SCHOTT

SHIPMENT LABEL INTEGRATION

PROJECT PLANNING

DEC 2022-JAN 2022

OVERALL DELIVERABLE SOLUTION – SOPHIC - SCHOTT

Features

1. Approval Stage from Production, QA and Shipment for FG Submission.
2. Label printing capabilities at the Production, QA and Shipment for FG Submission.
3. Retrieval of package details via scanning (Barcode) Capabilities for search unique ID of the packages.
4. Export document capabilities via work order and consolidation that is Receiving List and Due List .
5. Support dynamic label design that allow minimal low code adjustment of the layout.

Based of requirement submitted Shipment Label system reference R5 (submitted 20/10/222)

Objectives

1. Simplify the approval stage at packing and QC.
2. Utilize 100% WFS forms for the process.
3. Manage the label design as One system from Inner to Carton.
4. FOCUS on data INTEGRITY and SPEED.
5. Traceable approval method for further package investigation.
6. Allow maintainer to manage overall for update require by customer even without vendor support.

SOPHIC TEAMS & SCRUM METHODOLOGY

Product Architect
(PIC: Afifi)


1. Provide features list
2. Priority features time to market
3. Get feedback end user
4. Review & announce software release

Scrum QC Master
(PIC: Yowyih)


1. Provide updates to product manager
2. Ensure team done activity on time
3. Administrative all developers
4. Review the code/bugs/severity
5. Announce software release

In-House Developer (10 Full Time HC)
(PIC: Najmuddin, Azad, Elwyn, Yi Shin, Shahredza, Atiqah, Irfan, Khairuddin, Amar)

1. Ensure task completion done in timely manner
2. Update the code to GIT/repo everyday
3. Document task accordingly
4. Optimize time
5. Testing the code before merge and finally release

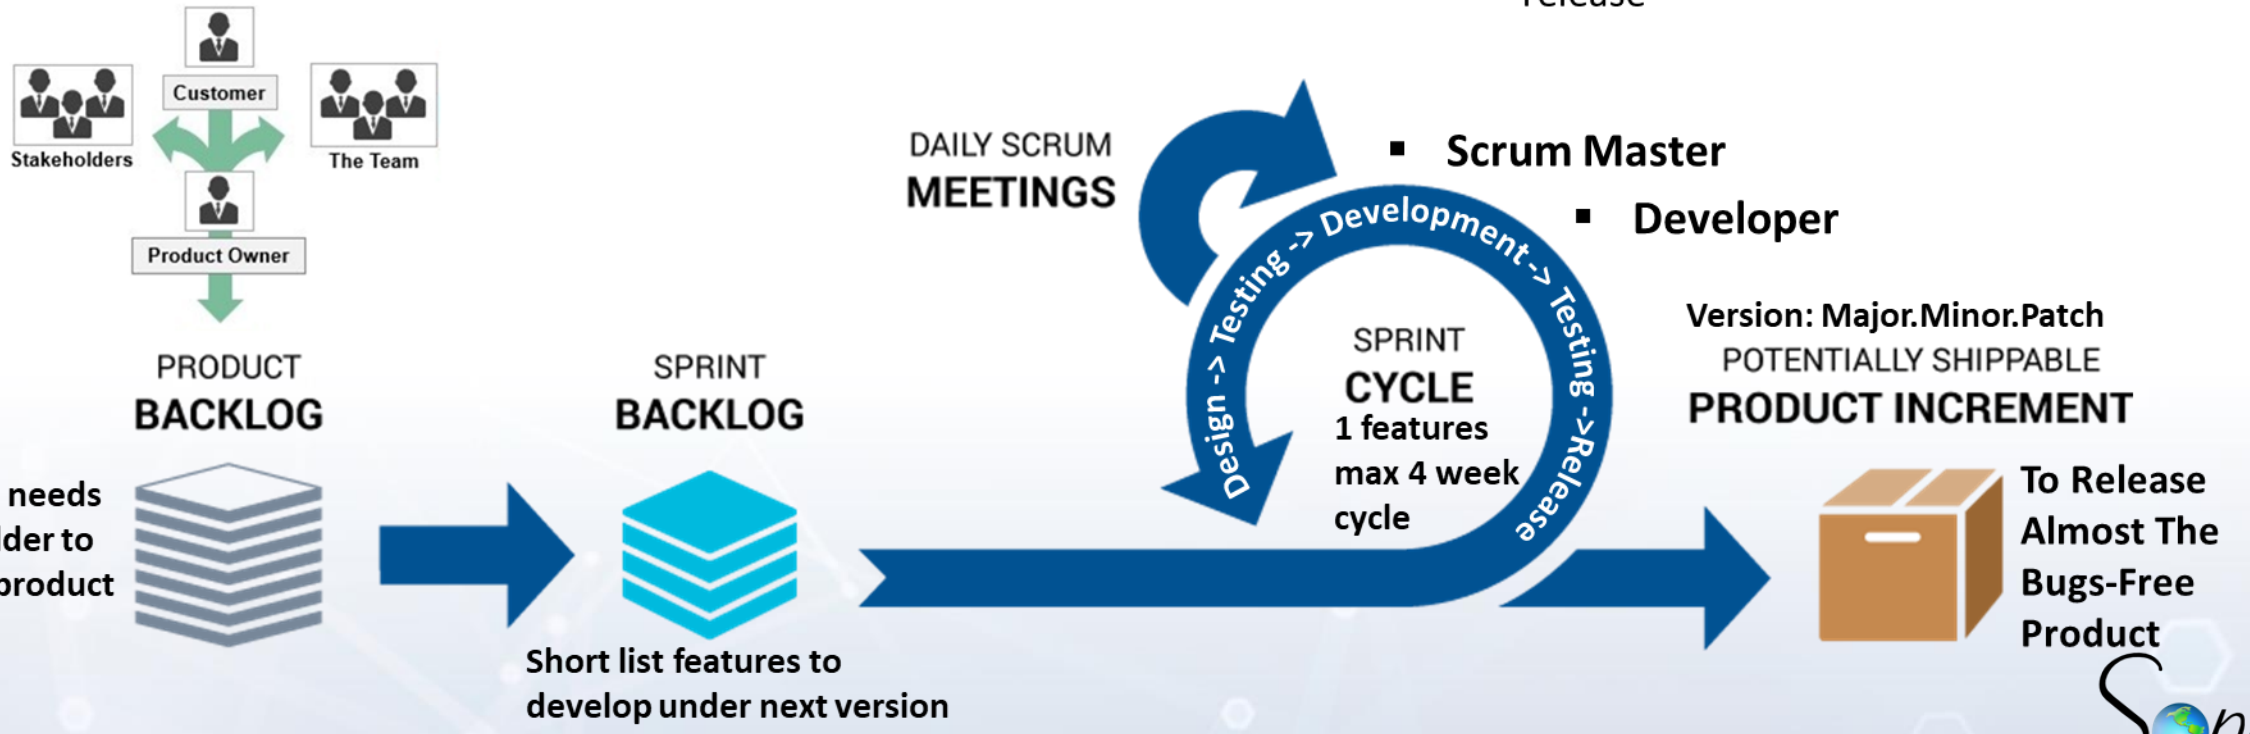


CURRENT CORE ARCHITECTURE – WFS

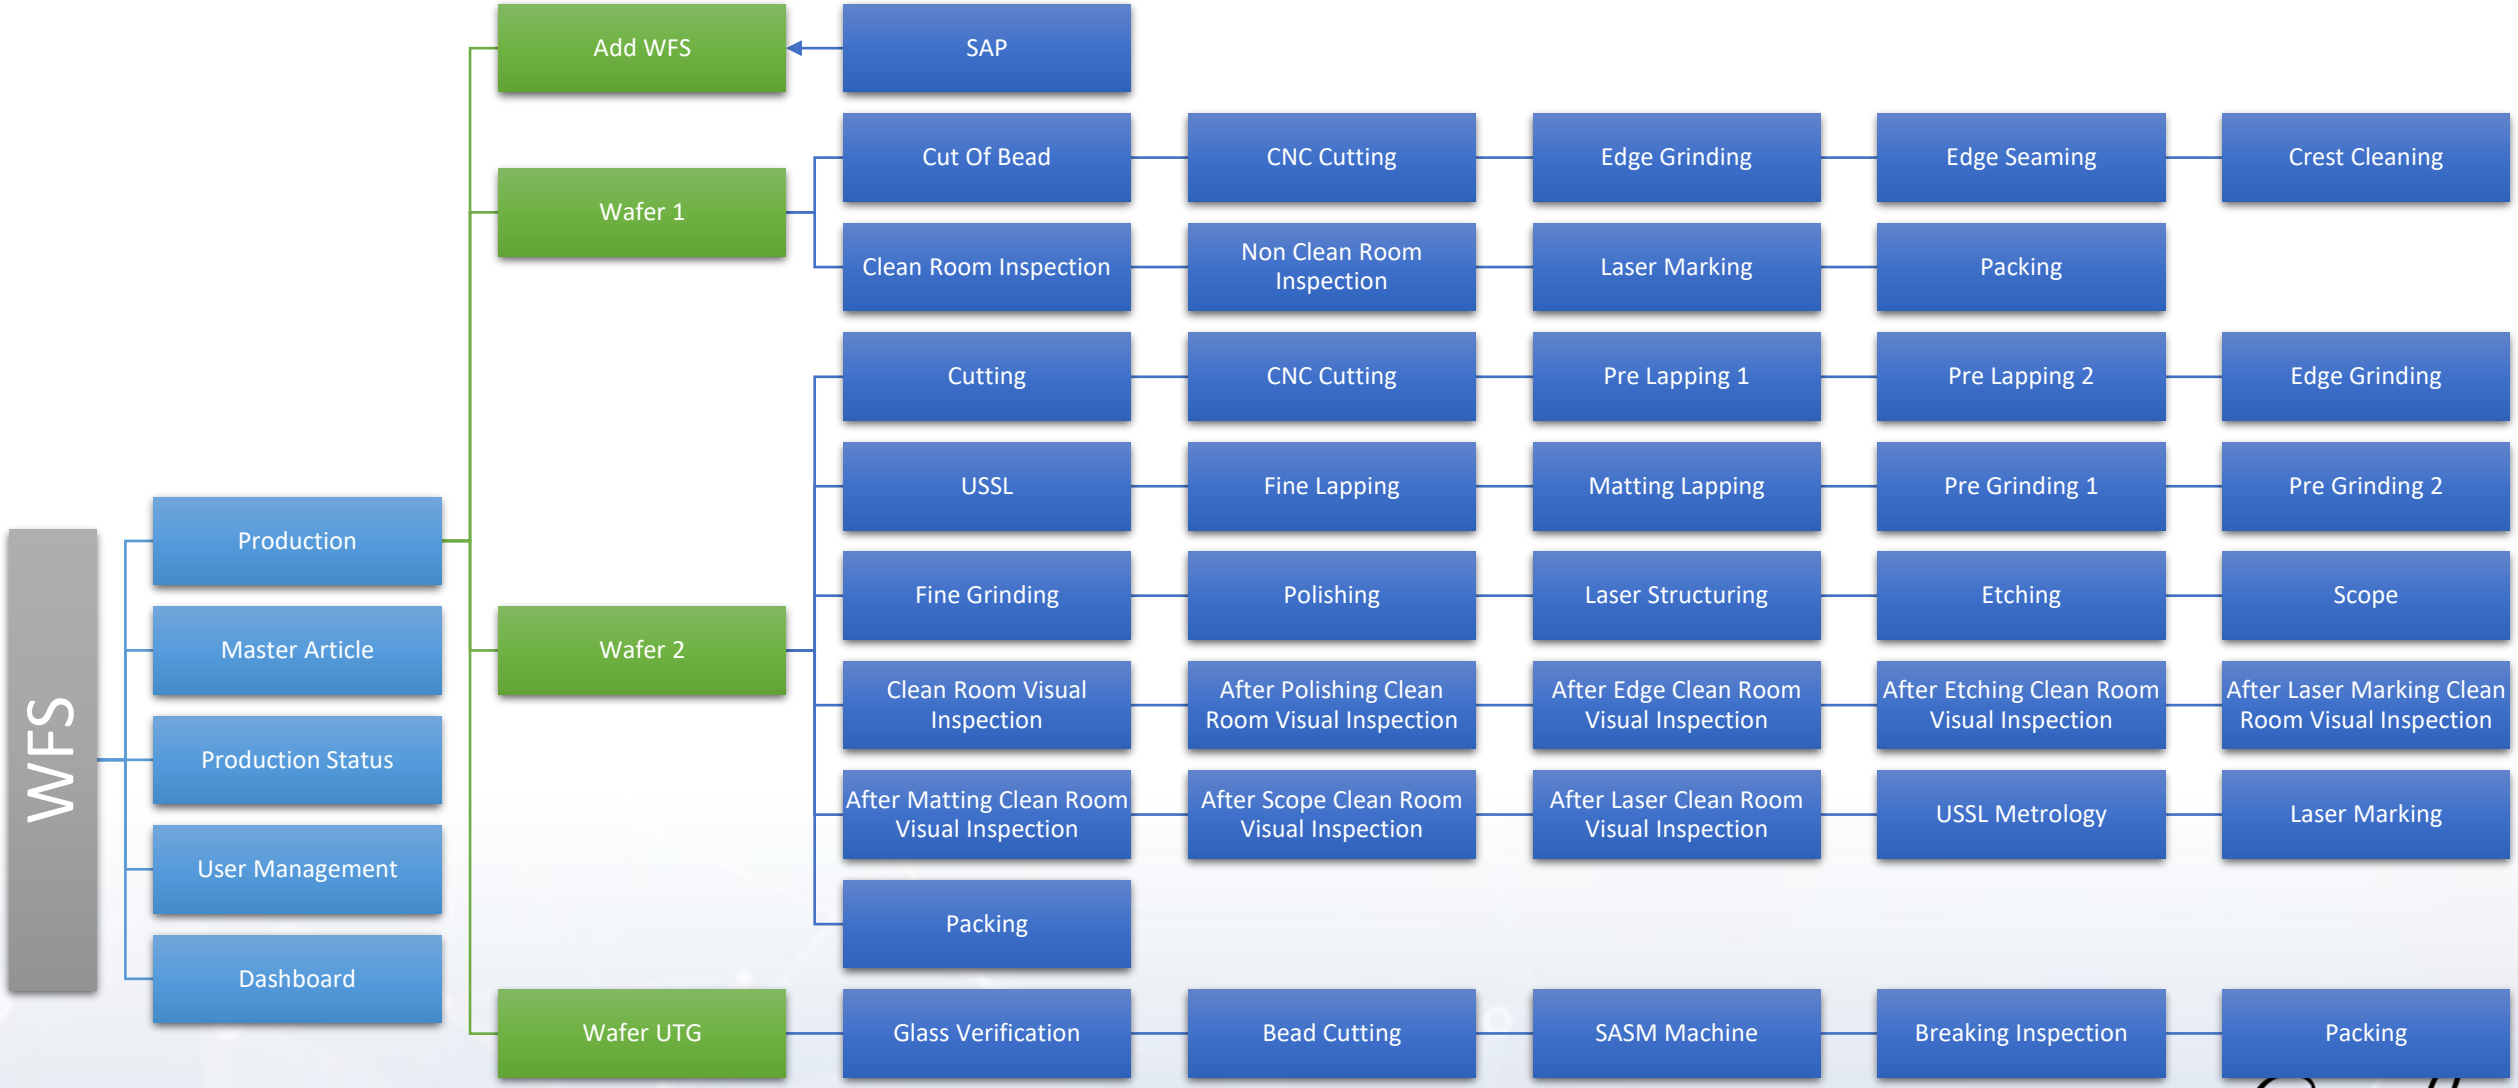


NEXT INTEGRATION – WFS + SHIPMENT




DATA FLOW – SHIPMENT – R5 (FINALIZED) – (1)

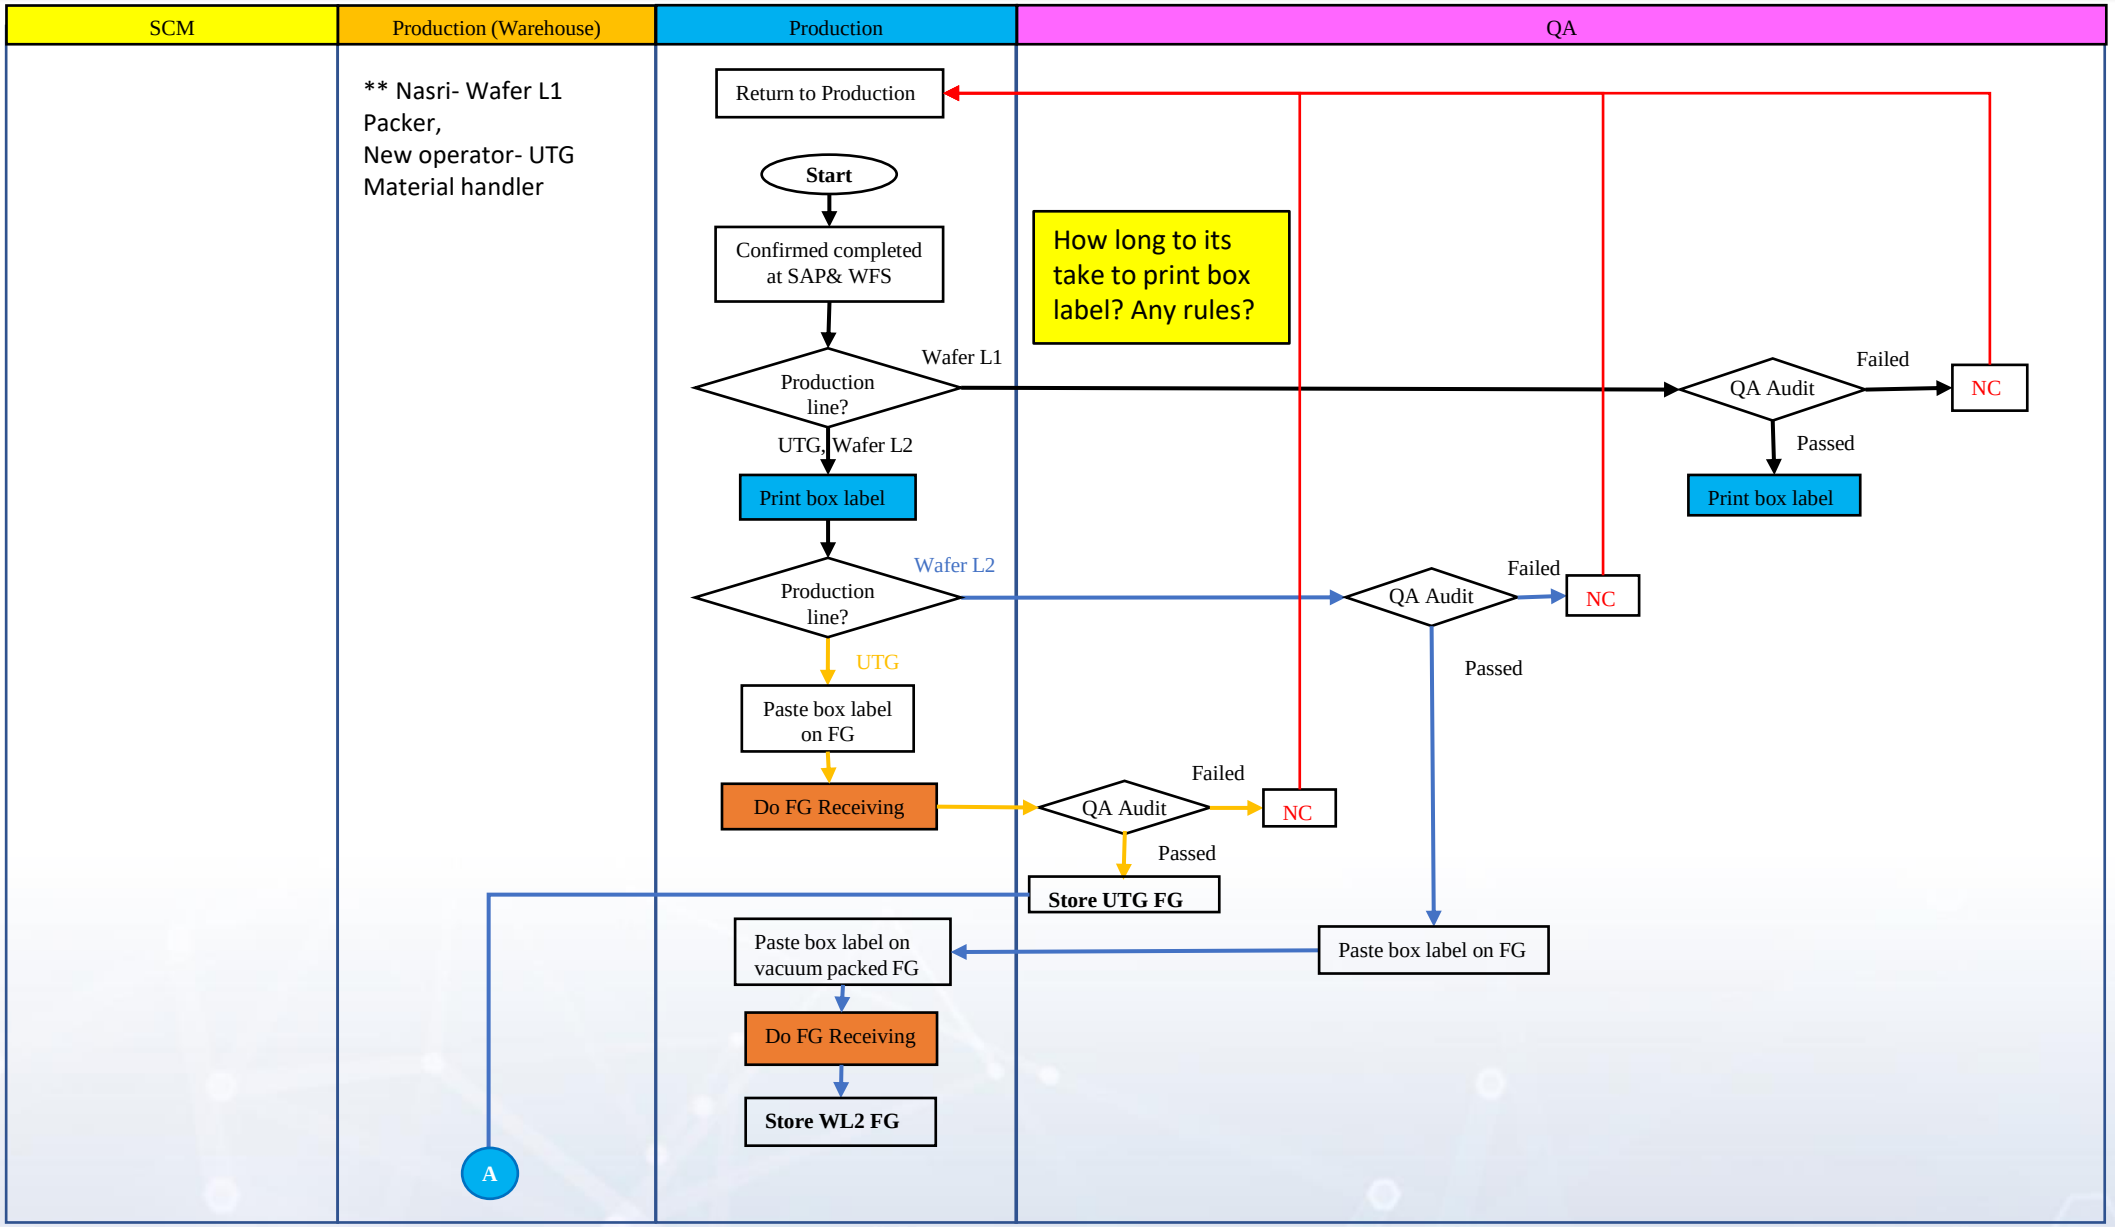


DATA FLOW – SHIPMENT – R5 (FINALIZED) – (2)

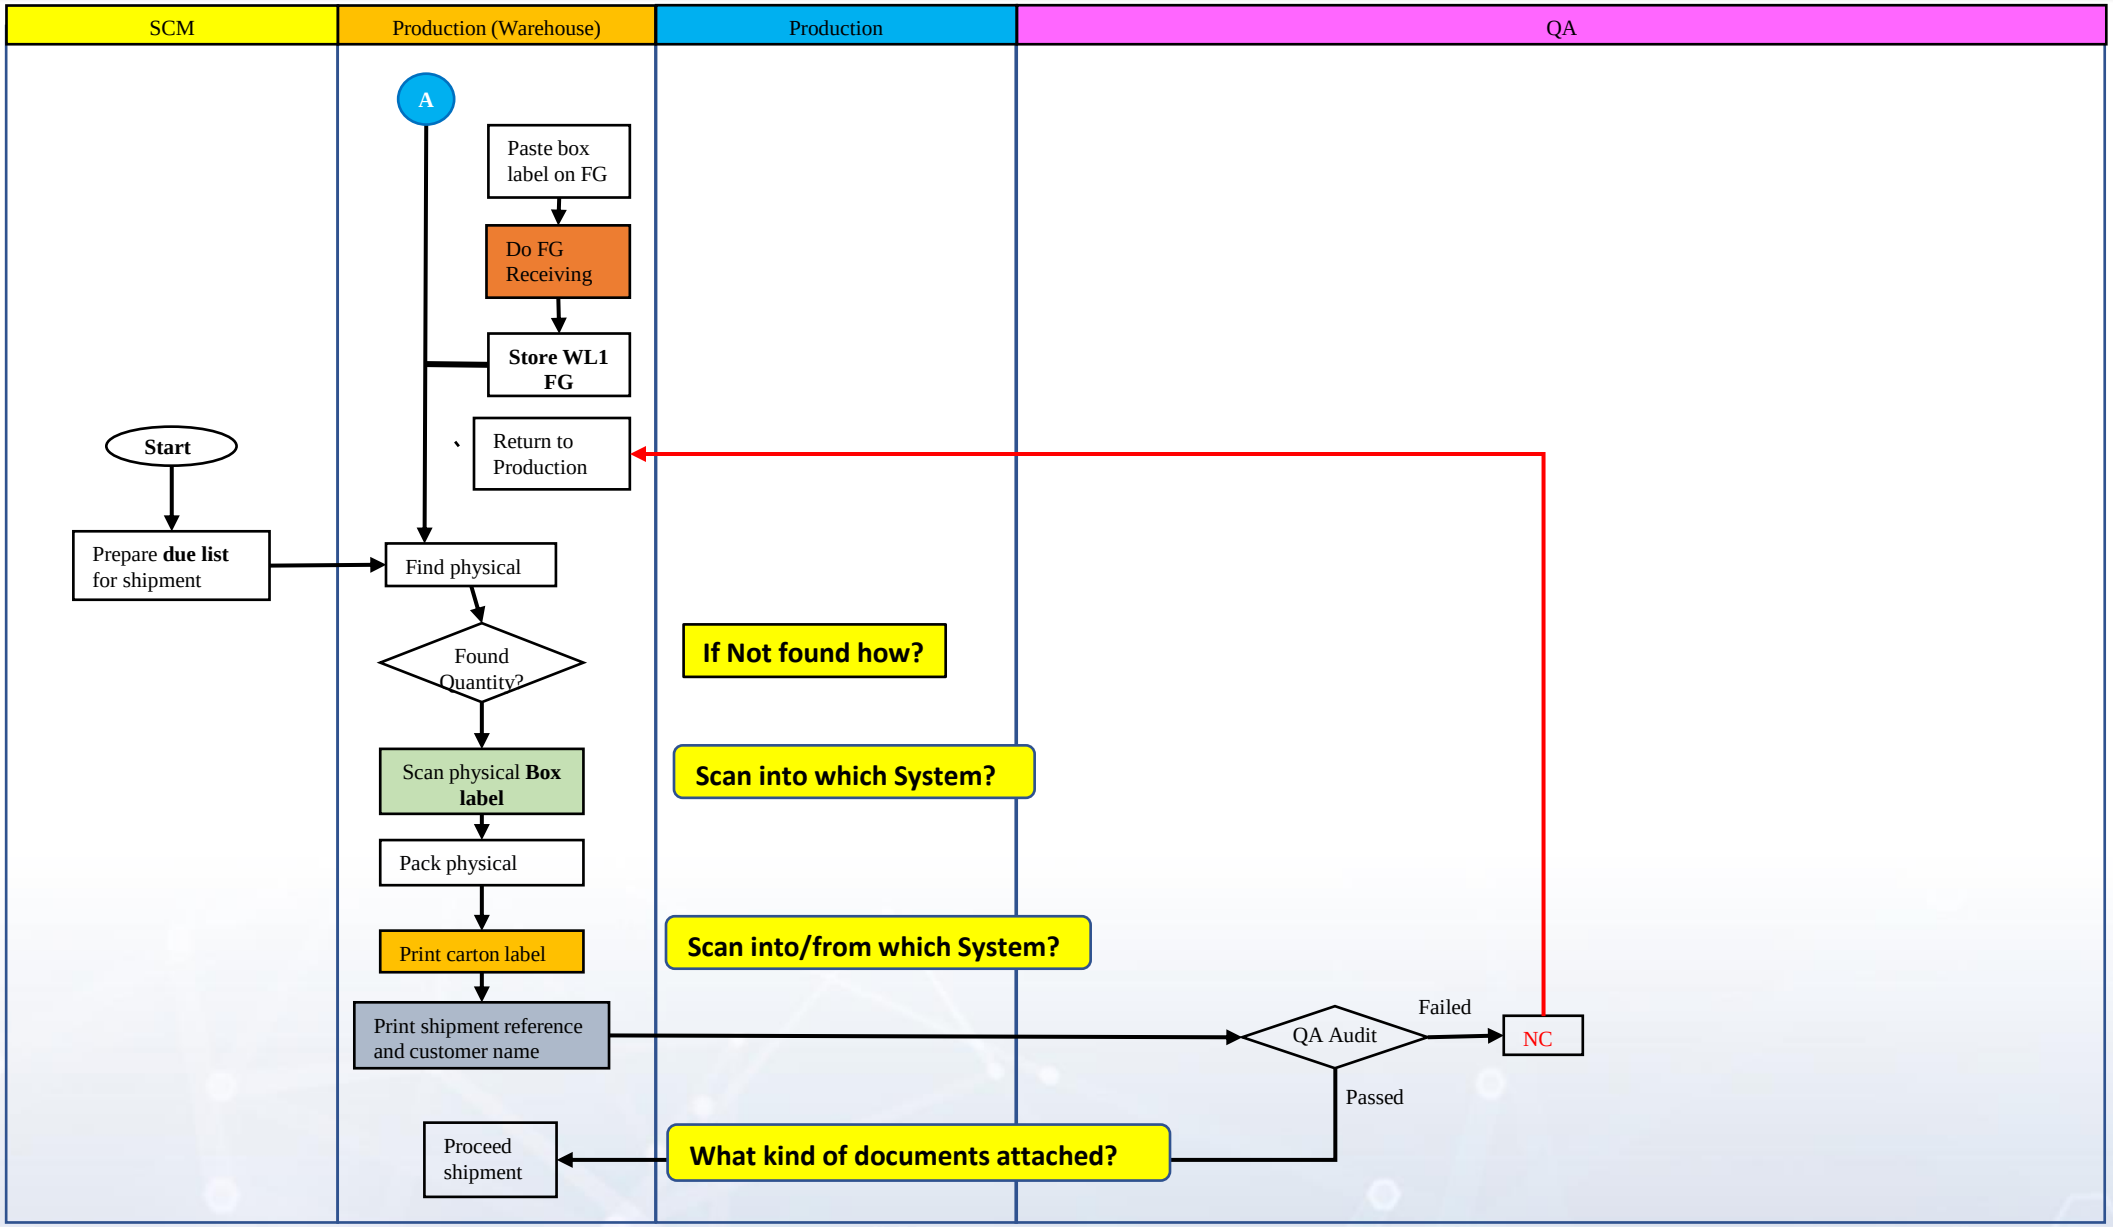


INTERFACE DESIGN – ADD SHIPMENT ROUTING

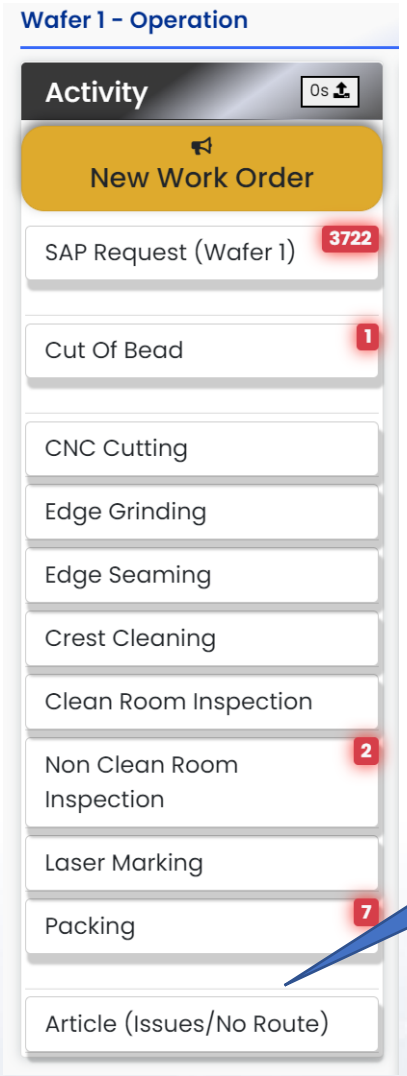

1. QA Audit (QA)
2. Finished Good (FG)
3. Receiving (RG)
4. Shipping (SG)

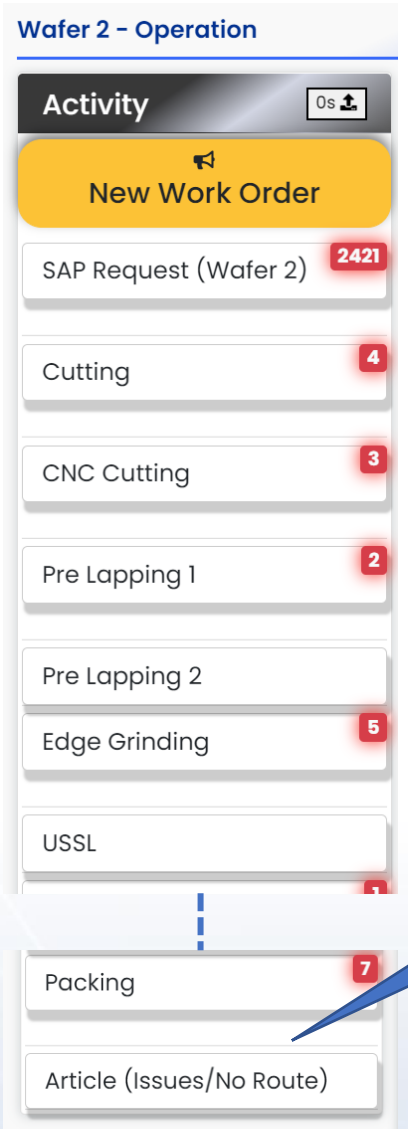

1. QA Audit (QA)
2. Finished Good (FG)
3. Receiving (RG)
4. Shipping (SG)

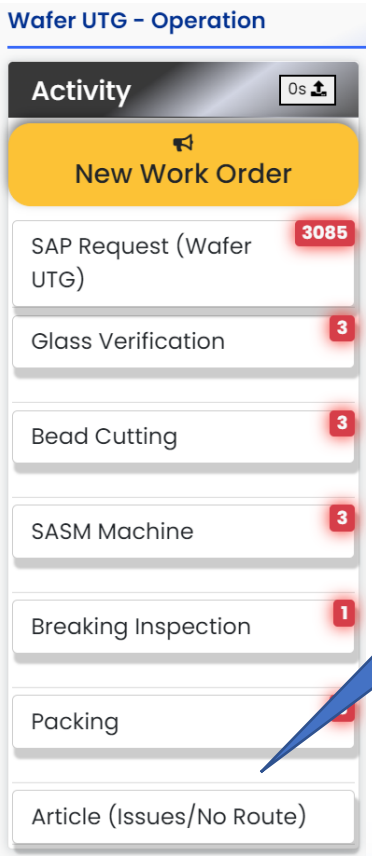


1. QA Audit (QA)
2. Finished Good (FG)
3. Receiving (RG)
4. Shipping (SG)

- Article Routing is IMPORTANT, maintainer must make sure all article are provide with the routing flow contained the codename for QA process.

INTERFACE DESIGN – REAL TIME LIST – QA AUDIT


- View Detail
- Search
- Sort (FIFO)

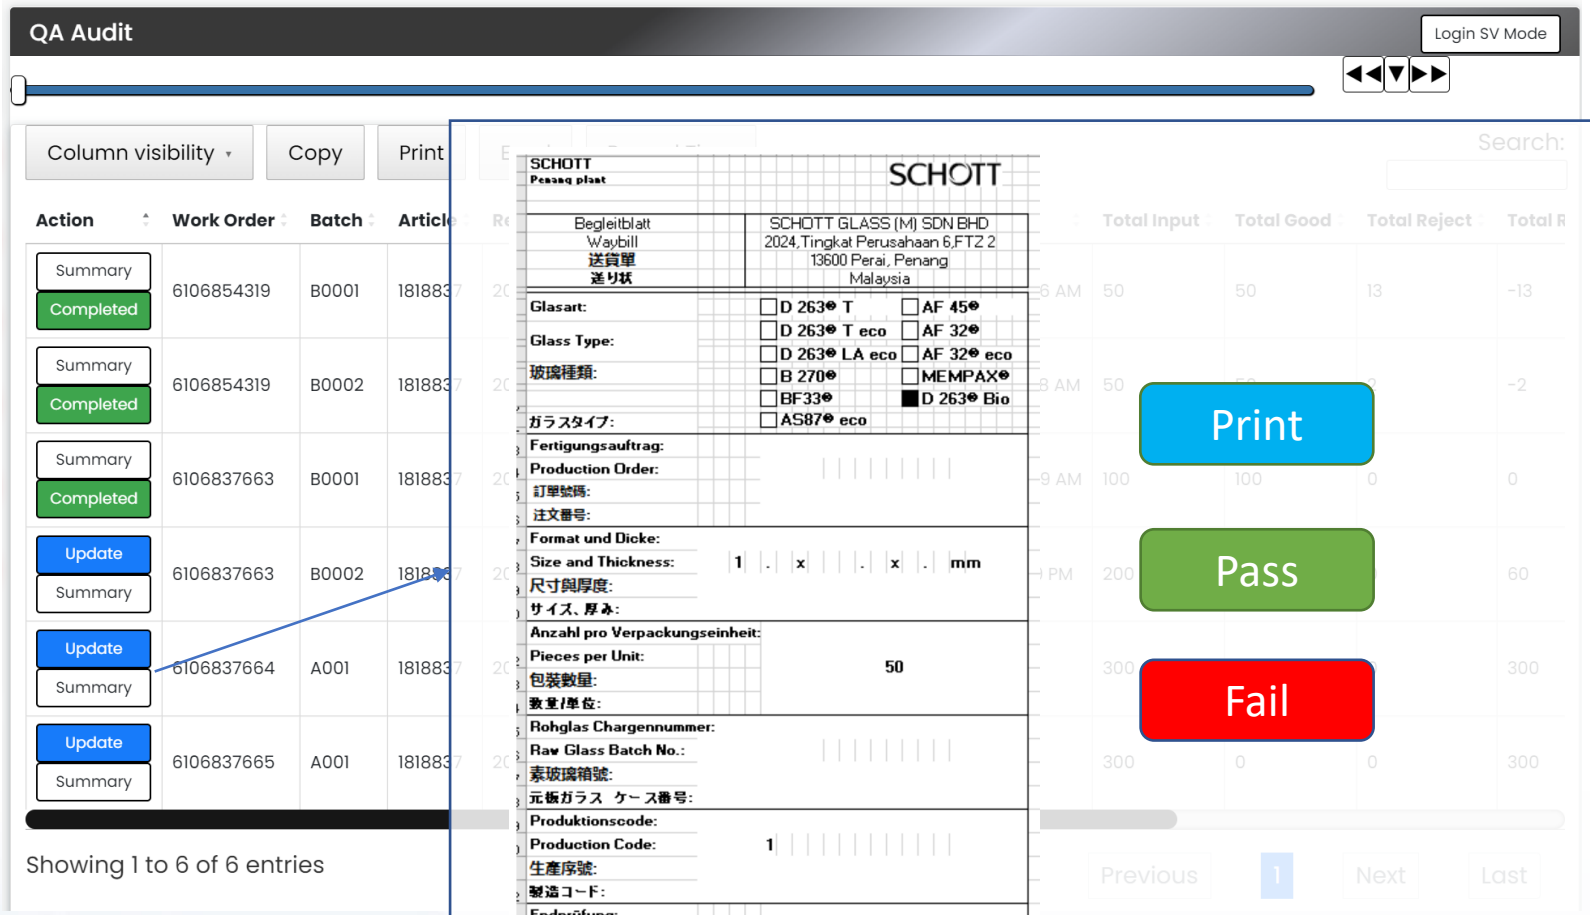

- Print Report
- Approval
  - Pass
  - Fail


INTERFACE DESIGN – REAL TIME LIST – FINISHED GOOD

- View Detail
- Search
- Sort (FIFO)

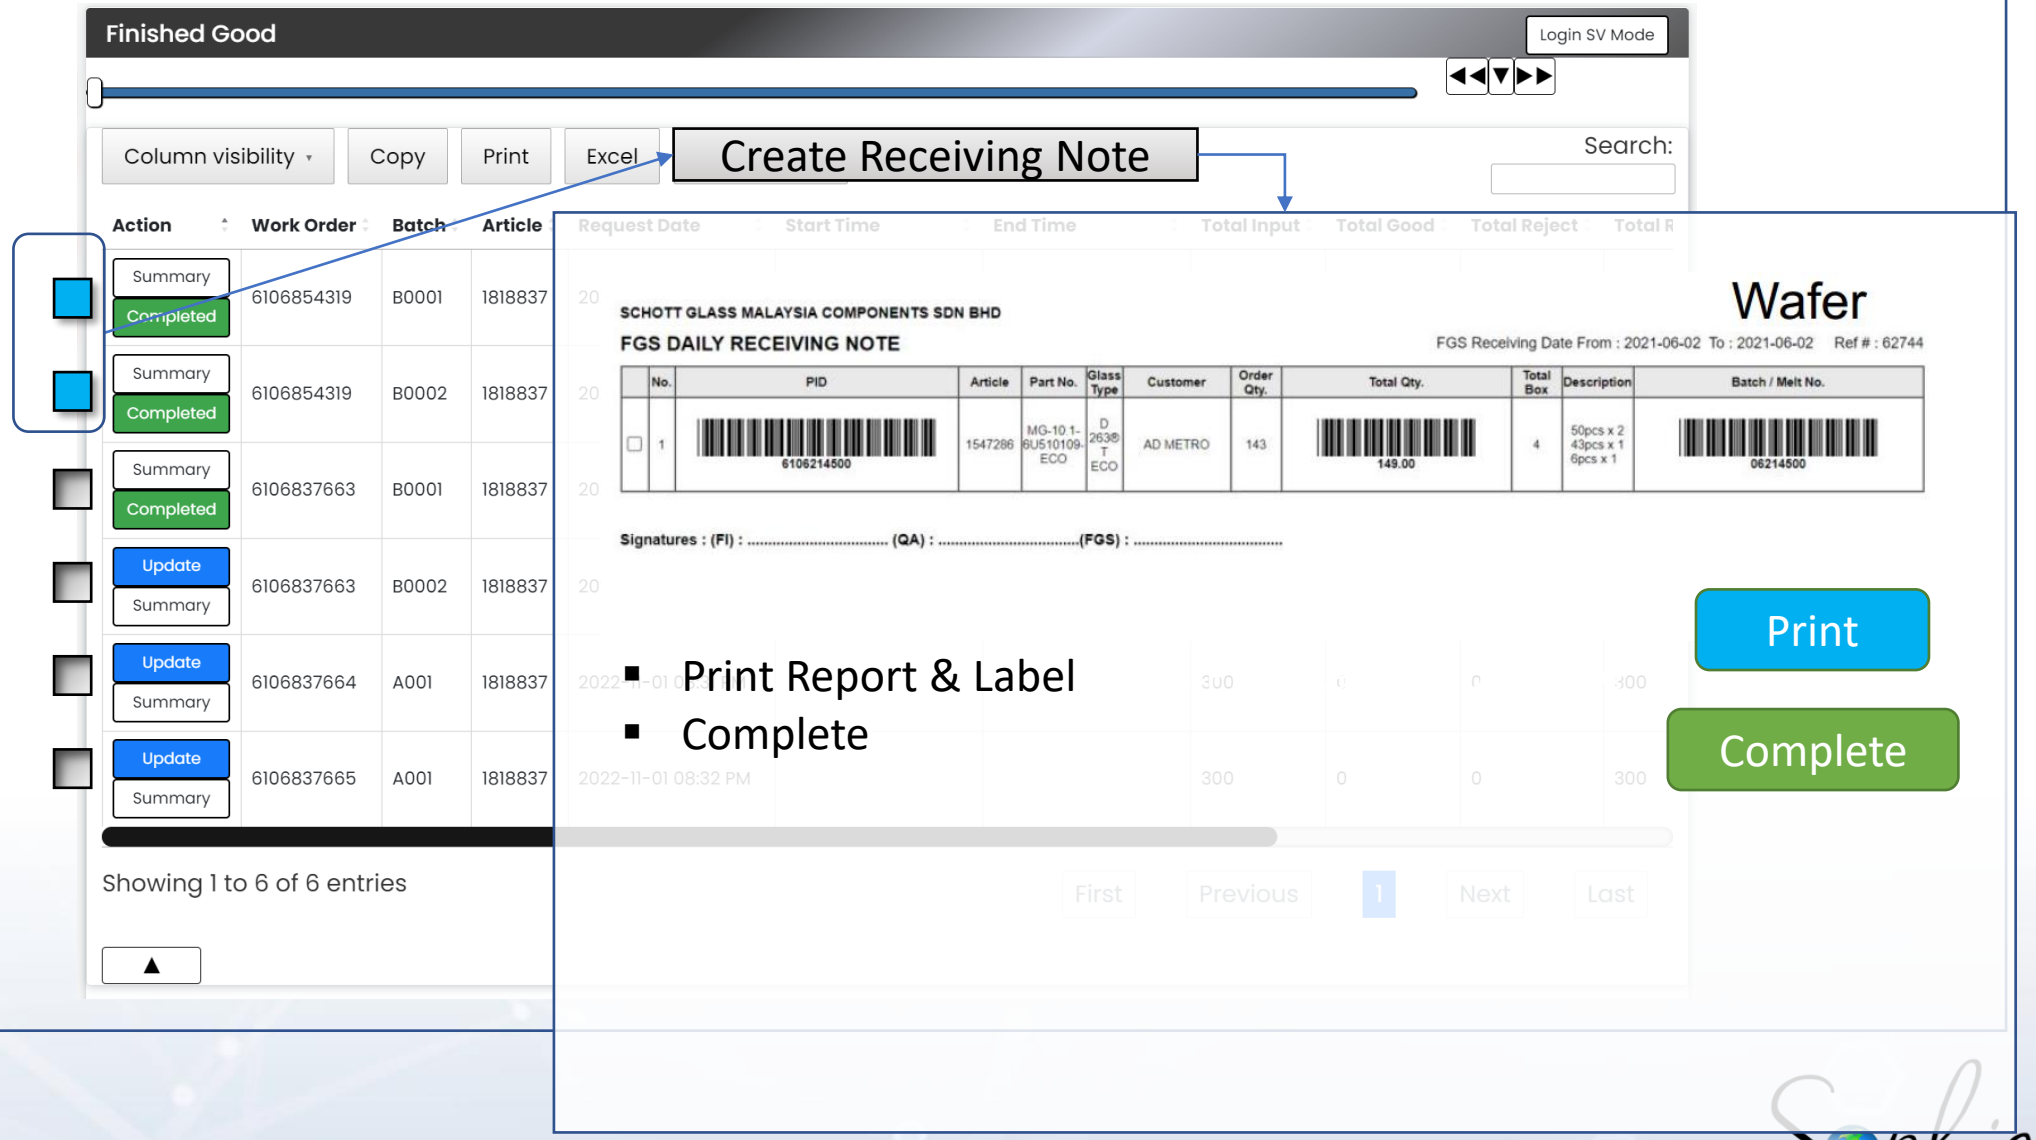

INTERFACE DESIGN – REAL TIME LIST – RECEIVING


- View Detail
- Search
- Sort (FIFO)

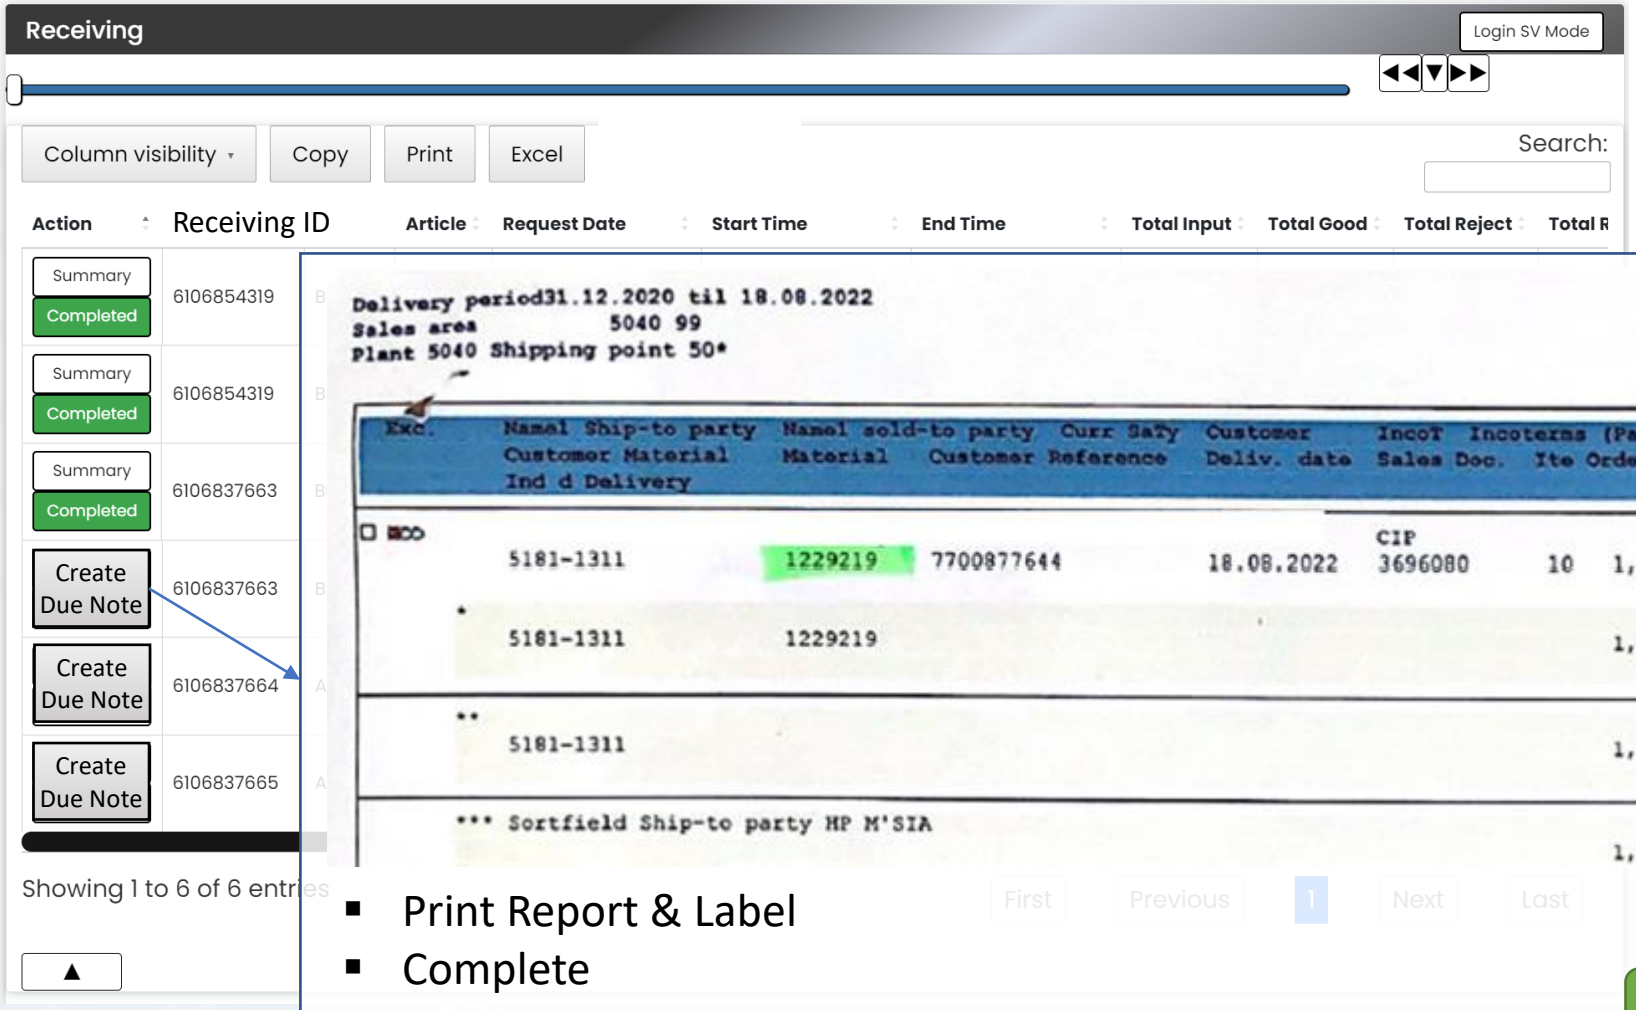

- Print Report & Label
- Complete

INTERFACE DESIGN – REAL TIME LIST – SHIPPING

- View Detail
- Search
- Sort (FIFO)

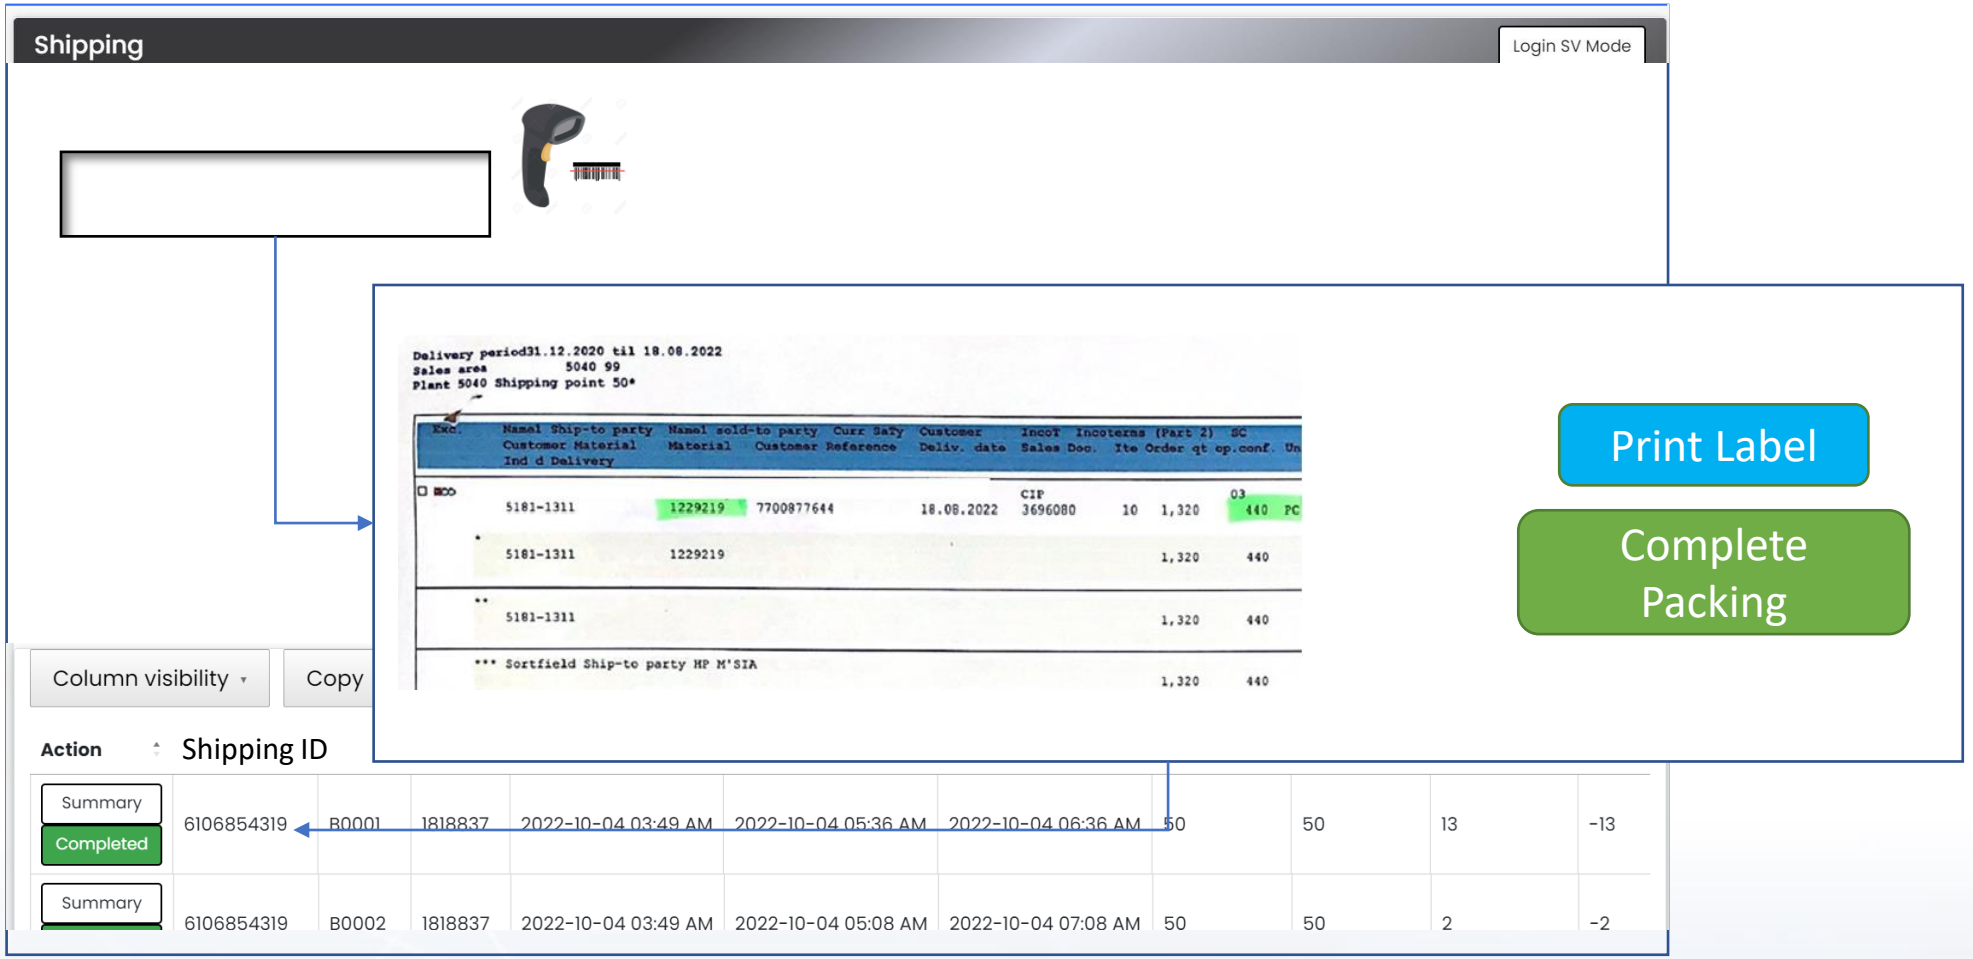

LABEL FORMAT – BASED OF SCHOTT REQUIREMENT

Actual release date	Order	Material	Description	Plant	Document	Customer name	Basic material	Shape
3/11/2022	6106629058	1844690	CD FI D 263® T eco Ø150x0.5 M PK FG	5040	UAB-D263-150X0.5-M	LTUAB	D 263® T eco	Cut Disc
3/11/2022	6106629060	1844691	CD FI D 263® T eco Ø150x1.0 M PK FG	5040	UAB-D263-150X1.0-M	LTUAB	D 263® T eco	Cut Disc
3/11/2022	6106631018	1504474	CD FI BF33 S1270105102 150x1 55175234	5040	S1270105102	BOSCH	BOROFLOAT33	Cut Disc
3/11/2022	6106631019	1807289	CD FI BF33 BG08R32B Ø100x0.8 EG W F P FG	5040	BG08R32B-TEST-2.2	DETDKEPC1	BOROFLOAT33	Round Disc with Hole
3/11/2022	6106631021	1800639	PL FI Mempax® 300x300x0.3 CB FG	5040	LPKF-MPX-300X300X0.3	DELPKFL&E	Mempax®	Plate
3/11/2022	6106631023	1824515	CD FI AF32®eco Ø150x0.5 M FG	5040	LPKF-AF32-150X0.5	DELPKFL&E	AF 32® eco	Cut Disc
3/11/2022	6106631024	1807289	CD FI BF33 BG08R32B Ø100x0.8 EG W F P FG	5040	BG08R32B-TEST-2.2	DETDKEPC1	BOROFLOAT33	Round Disc with Hole
3/11/2022	6106631026	1842150	PL FI AS90eco 550x370x0.032 CL FG	5040	LJ64-06535A	KRSDC	AS 90 eco	Plate
3/11/2022	6106631027	1842150	PL FI AS90eco 550x370x0.032 CL FG	5040	LJ64-06535A	KRSDC	AS 90 eco	Plate
3/11/2022	6106631028	1842150	PL FI AS90eco 550x370x0.032 CL FG	5040	LJ64-06535A	KRSDC	AS 90 eco	Plate
3/11/2022	6106631029	1842150	PL FI AS90eco 550x370x0.032 CL FG	5040	LJ64-06535A	KRSDC	AS 90 eco	Plate
3/11/2022	6106631204	1269921	PL FI D 263® T eco 440x410x0.145 CB FG	5040	1269921-SGMC	SGMC	D 263® T eco	Plate

Material
Document
To be filled in
Basic material
Customer name
Order

Article: **1269921**
Part No: **1269921-SGMC** Last 8 digit of Order
Prod Code: **2007031662833** Batch No: **06631204**
Glass-Type: D 263® T eco Art. Desc.: PL FI D 263® T eco 440x410x0.145 CB FG Description
Customer: SGMC
PID: **6106631204** Quantity: **10** PCs
To be filled in
RoHS COMPLIANCE
B126992100663120400010

For barcode batch (general)

Individual	1	2	3	4	5	6	7	8	9
Explanation	Batch No. (last 8 digit from Order)								
Example	0	0	6	6	3	1	2	0	4

For barcode batch (Viavi)

Cumulative	1	2	3	4	5	6	7	8
Individual	1	2	3	4	5	6	1	2
Explanation	Label printed out date (YYMMDD)						Running serial by date by WO	
Example	2	2	0	2	0	4	0	1

For barcode Mfg date& CID (Viavi)

Cumulative	1	2	3	4	5	6	7	8	8	9	10	11	12	13	14
Individual	1	1	2	3	4	5	6	7	8	9	10	1	2	3	4
Explanation	Mfg location (Malaysia)	Label printed out date (YYMMDDHHMM)										Running serial by date			
Example	M	2	2	0	2	0	4	1	2	3	4	0	0	0	1

Susgested to change: For barcode (inner + outer)

Cumulative	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
Individual	1	2	3	1	2	3	4	5	6	7	1	2	3	4	5	6	7	8	9	1	2	3	4	5
Explanation	Unique code			Article						Barcode batch									Quantity					
Example	9	9	9	1	2	6	9	9	2	1	0	0	6	6	3	1	2	0	4	0	0	0	1	0

LABEL DESIGN – CURRENT VARIATION

Standard+LMS




Xintec



- Add barcode for quantity
- Add Part No. + Batch + Serial No with barcode

SDC + Space X (QR+



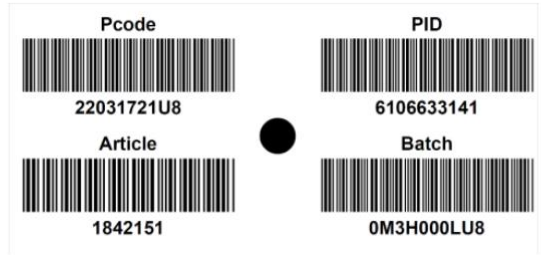

Qualcomm



- Prod.Code not display
- Add barcode for Part No and Batch No

Viavi



- Prod.Code not display
- Add barcode for Part No and Batch No
- Add Mfg.Date & CID with barcode

LABEL DESIGN – DESIGNER MANAGEMENT

```
^XA

^FX Top section with logo, name and address.
^CF0,60

^FO50,50
^GB100,100,100^FS

^FO75,75
^FR
^GB100,100,100^FS

^FO93,93
^GB40,40,40^FS

^FO220,50
^FDSCHOTT, Inc.^FS

^CF0,30
^FO220,115
```

Labelformat:

102 mm (4.0 inches) 152 mm (6.0 inches) 8 dpmm (203 dpi)

Render

Printer IpAddress:

Print


SCHOTT, Inc.
1000 Malaysia
Penang TN 38102
Qualcomm

John Doe
100 Main Street
Springfield TN 39021
United States (USA)

Permit
123456


12345678

- Allow maintainer to create a template for customers via tool Label Designer built on the system.
- Allow to copy template and create duplication
- Capabilities are limited for position of label, sizes, simple graphics (Line, Rectangle)
- Support barcode design Code39 and QR Code.
- Limitation: Not include capabilities to add new parameters

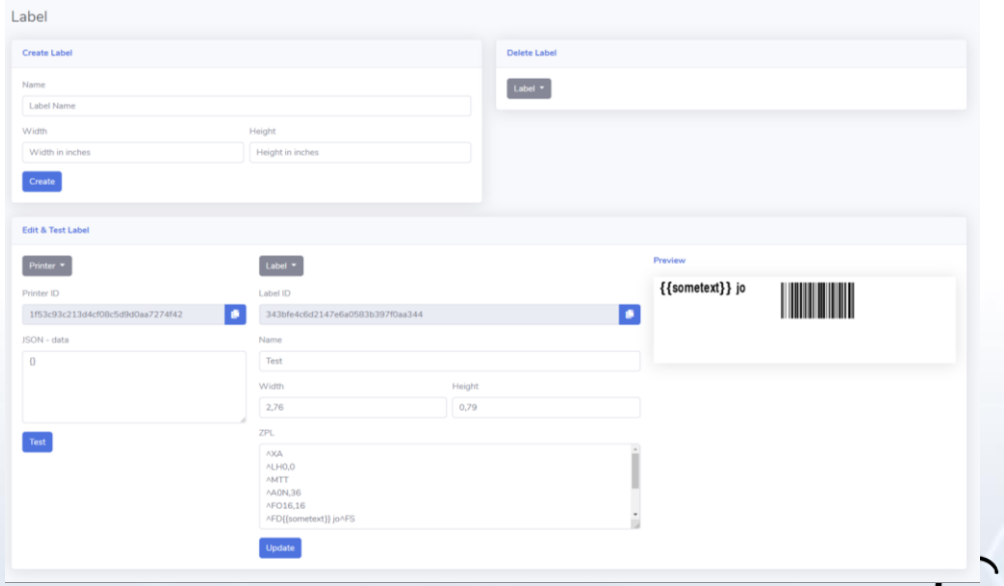

SUMMARY WFS + SHIPMENT

WBS	Tasks	Start	End	PIC	Duration (Days)	Complete %	Days Complete	Days Remaining
							Month	
							Days	
1	**Development**	**21/10/2022**	**30/12/2022**	**Sophic**	**67**	**25%**	**6**	**64**
1.1	Finalizing Requirements	21/10/2022	31/10/2022	Sophic	32	50%	6	30
1.1.1	Finalizing Requirements	21/10/2022	21/10/2022	Afifi	1	100%	5	0
1.1.2	PO Received	1/10/2022	31/10/2022	Michelle	31	0%	1	30
1.2	System Development	21/11/2022	30/12/2022	Sophic	35	0%	0	34
1.2.1	Enhancement to Label Designer	21/11/2022	30/11/2022	Afifi	10	0%	0	10
1.2.2	Production Flow Approval Logic & Label	1/12/2022	12/12/2022	Afifi	12	0%	0	12
1.2.3	System Release & Presentation - v0.5	13/12/2022	13/12/2022	Afifi	1	0%	0	1
1.2.4	System Deployment (Onsite) - v0.7	20/12/2022	20/12/2022	Najmuddin	1	0%	0	0
1.2.5	Shipment Approval Logic & Label	14/12/2022	19/12/2022	Najmuddin	6	0%	0	6
1.2.6	RPA QC Testing - v0.9	21/12/2022	24/12/2022	Najmuddin	4	0%	0	4
1.2.7	System deployment (Onsite) - v1	30/12/2022	30/12/2022	Najmuddin	1	0%	0	1
2	**Training and UAT Sign-Off**	**14/12/2022**	**20/1/2023**	**Team**	**33**	**0%**	**0**	**33**
2.1	UAT	14/12/2022	13/1/2023	Team	27	0%	0	27
2.1.1	Regression Testing & Enhancement (Internal)	14/12/2022	19/12/2022	QC Software	6	0%	0	6
2.1.2	Production Testing & Enhancement (OnSite)	21/12/2022	29/12/2022	QC Software	9	0%	0	9
2.1.3	Fine Tuning based on Feedback (OnSite)	31/12/2022	6/1/2023	QC Software	7	0%	0	7
2.1.4	UAT Checklist Buyoff (OnSite)	9/1/2023	13/1/2023	QC Software	5	0%	0	5
2.2	Training	16/1/2023	16/1/2023	Team	2	0%	0	2
2.2.1	On-site Training (OnSite)	16/1/2023	16/1/2023	Afifi	1	0%	0	1
2.2.2	Manual & Documentation	16/1/2023	16/1/2023	Afifi	1	0%	0	1
2.3	Go-Live	17/1/2023	20/1/2023	Team	4	0%	0	4
2.3.1	Production Live (OnSite)	17/1/2023	17/1/2023	Team	1	0%	0	1
2.3.2	Delivery Order Signed	18/1/2023	20/1/2023	Michelle	3	0%	0	3
3	**Post-Services**	**20/1/2023**	**1/8/2024**	**Team**	**2 years**	**0%**	**~**	**~**

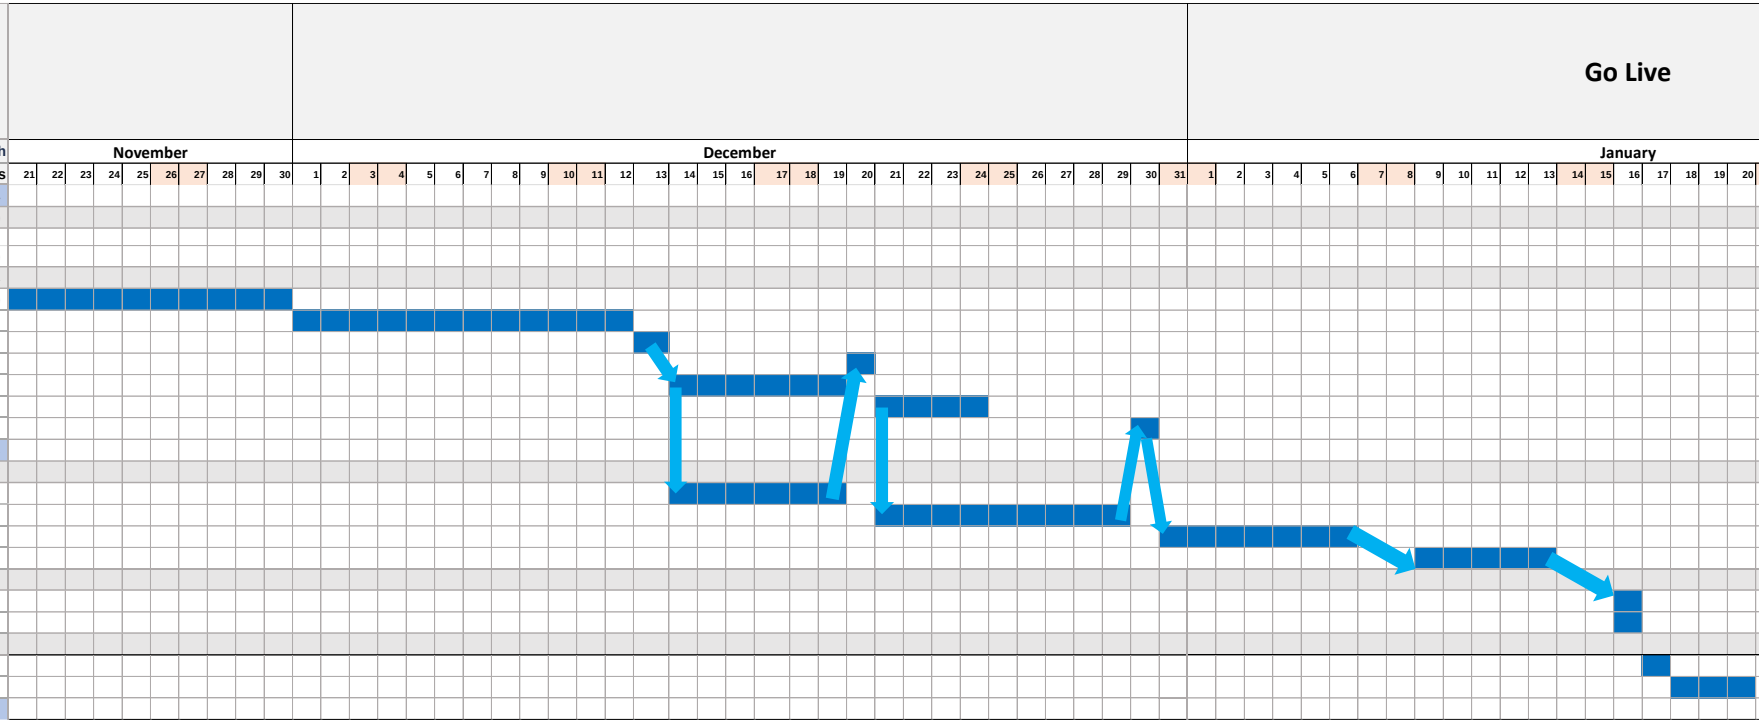



Excel file will send every week.

OR

https://docs.google.com/spreadsheets/d/1DWIdAWbKcseNNLz0qhuN1e8zQtIfnton/edit?usp=sharing&ouid=114769912323975083225&rtpof=true&sd=true

SUMMARY WFS + SHIPMENT

- The scope of work define are based of the R5 discussion.
- However there is not inclusive with data update Automatically to SAP.
- SCHOTT need to observe the current server performance (DB storage & memory) once the new system on the production server.
- Date Deliverables (Timeline):
  1. Development (15/11/2022 – 30/12/2022)
  2. Release v0.5 (1/1/2023)
  3. Feedback & Fine Tuning (1/1/2023 – 15/1/2023)
  4. Release v0.6 (16/1/2023)
  5. Feedback & Fine Tuning (16/1/2023 – 20/1/2023)
  6. Release v0.7 (21/1/2023)
  7. Feedback & Fine Tuning (21/1/2023 – 25/1/2023)
  8. Release v0.8 (26/1/2023)
  9. UAT1 & Fine Tuning (26/1/2023 – 29/1/2023)
  10. Release v0.9 (30/1/2023)
  11. UAT2 & Fine Tuning (26/1/2023 – 29/1/2023)
  12. Complete Version v1.0 (30/1/2023)
